

ANDERSON- SHIRO 2024 BOND PROGRAM


STATUS REPORT

March 2026

FINANCIAL UPDATE

Program Budget	\$60,000,000	Job Costs to Date	\$3,951,378
Commitments	\$43,153,206	Uncommitted Costs	\$16,846,794

Project	Budget	Commitment Costs	Job Cost to Date	Percent Complete	Project Phase	Anticipated Completion Date
Package 1 New Elementary School	\$53,800,000	\$40,592,882	\$2,858,795	5%	Construction	Spring 2027
Package 2 Access Road	\$2,500,000	\$2,250,770	\$1,056,894	42%	Construction	Spring 2026
Package 3 Renovations to Existing ES	\$3,700,000	\$309,553	\$35,689	1%	Design	Summer 2027

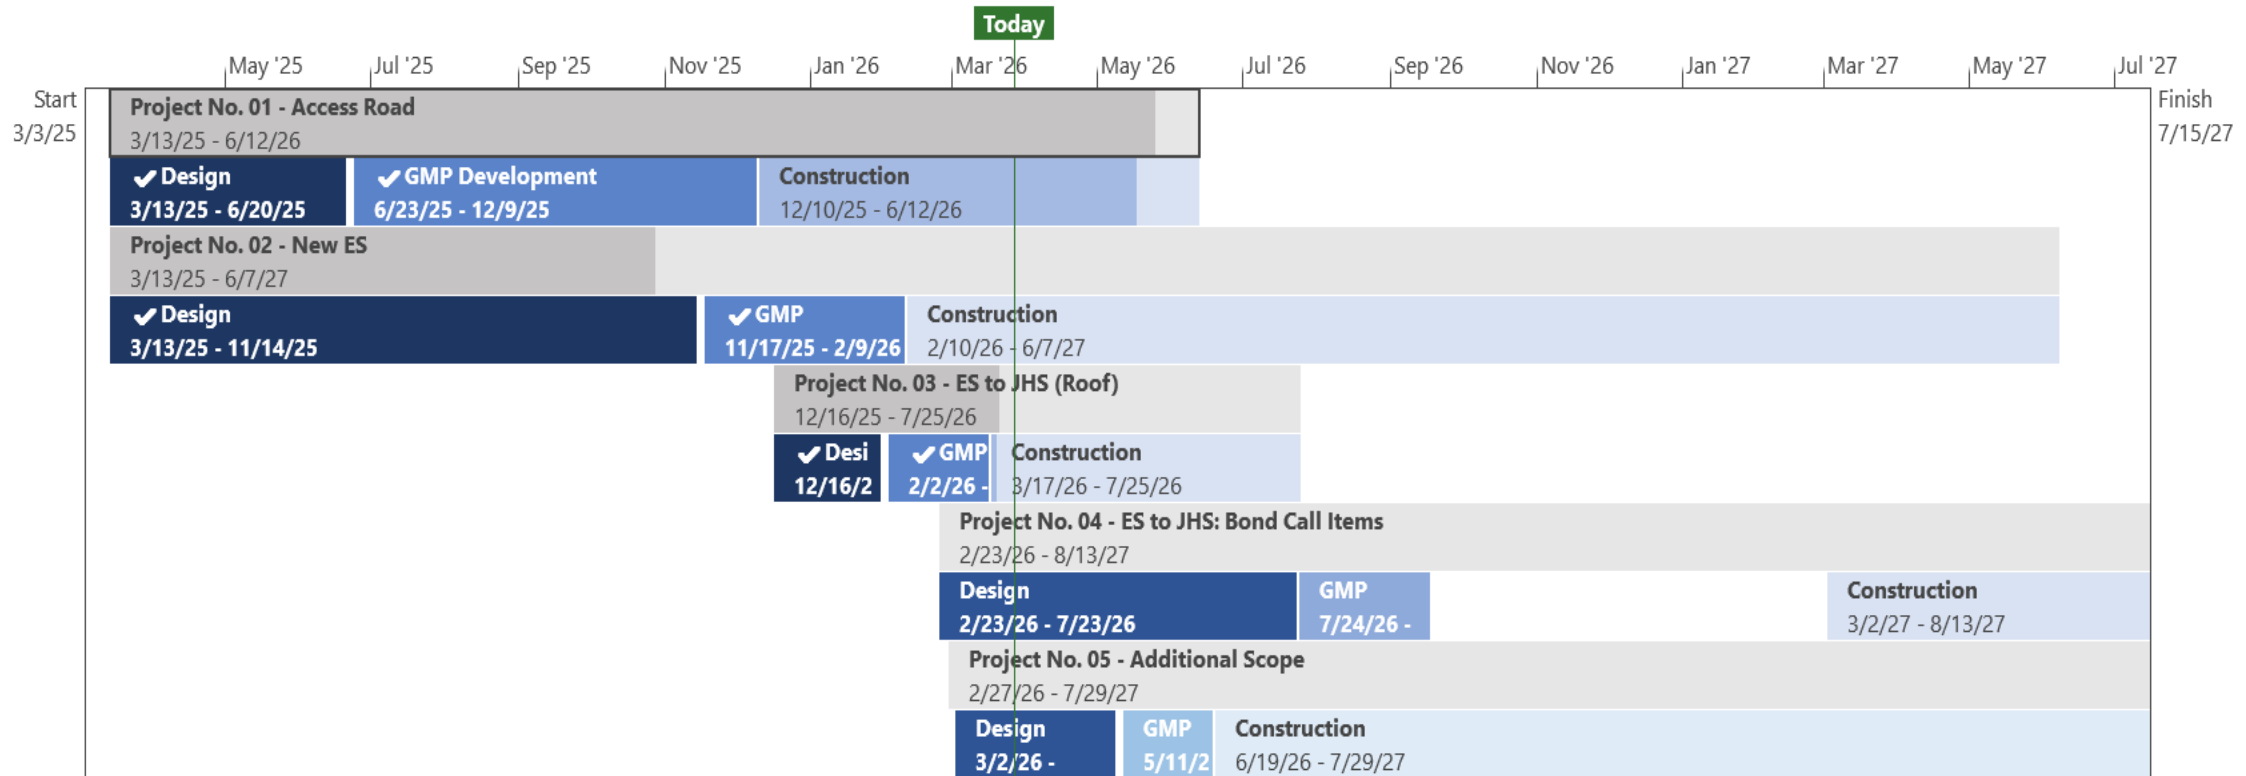

ASCISD 2024 Bond



STATUS UPDATES

- New Elementary School
 - Mobilization began Feb. 11
 - Site Clearing in progress
 - Fill dirt ongoing until April 3
- Access Road
 - Compaction, Rebar, Forms, Concrete pours complete
 - Project roughly 98% complete
 - Work will be complete April 30, and open to public August 2027
- Renovations to Existing ES
 - Re-roof bid negotiations began Feb. 27, currently in process

PROJECT PHOTOS & RENDERINGS



Access Road Behind HS



New ES Site Clearing

