

# ANDERSON- SHIRO 2024 BOND PROGRAM

## STATUS REPORT


### January 2026

#### FINANCIAL UPDATE

Program Budget	\$60,000,000	Job Costs to Date	\$2,377,940
Commitments	\$6,717,555	Uncommitted Costs	\$53,282,445

Project	Budget	Commitment Costs	Job Cost to Date	Percent Complete	Project Phase	Anticipated Completion Date
Package 1 New Elementary School	\$53,800,000	\$4,157,232	\$2,186,612	4%	Permitting	Spring 2027
Package 2 Access Road	\$2,500,000	\$2,250,770	\$172,500	7%	Construction	Spring 2026
Package 3 Renovations to Existing ES	\$3,700,000	\$309,553	\$18,828	1%	Design	Summer 2027

#### SCHEDULE

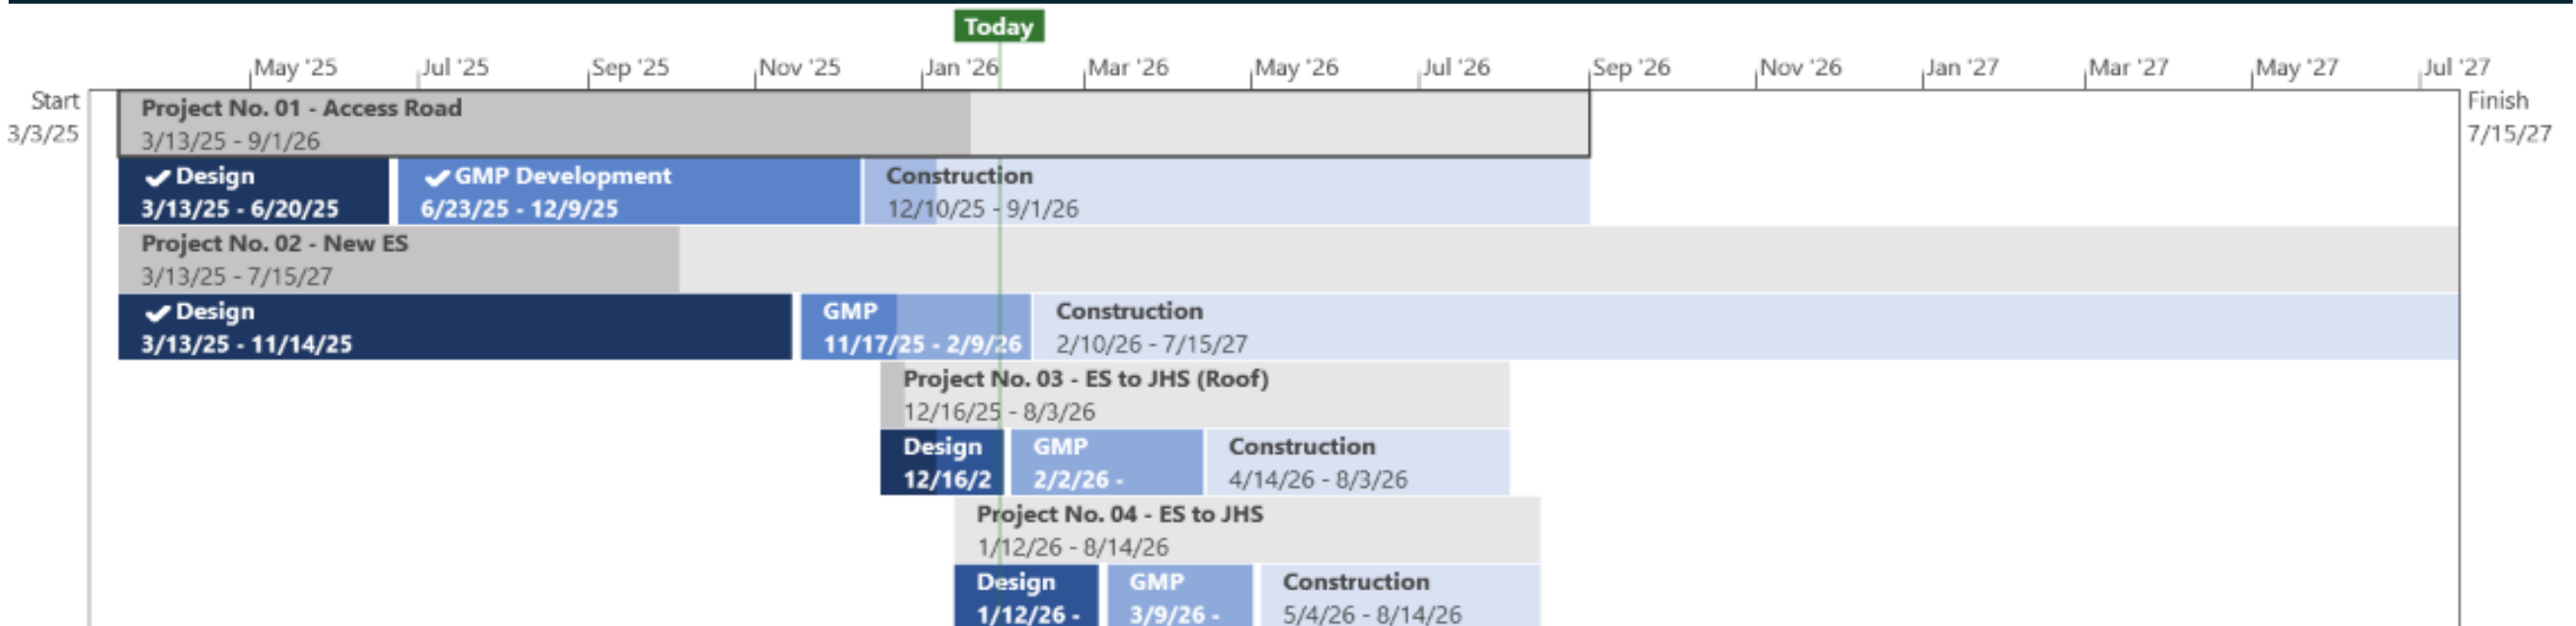

## STATUS UPDATES

- New Elementary School
  - GMP consideration of approval at Feb. 9 meeting
- Access Road
  - Clearing, grubbing, grading, lime, crossings, and road base complete
  - Project roughly 50% complete
  - Rebar, forms, concrete to begin last two weeks of Feb.
- Renovations to Existing ES
  - Re-roof design was completed and issued to the contractor for bidding Jan. 30

## PROJECT PHOTOS & RENDERINGS



**West Side of HS/JHS**



**Front Entrance Rendering**

