



# 2025 BOND PROGRAM STATUS REPORT



REPORTING PERIOD		AS OF:	
		Aug 31, 2025	
Program Budget	\$60,000,000	Job Cost to Date	\$865,574
Commitments	\$4,552,100		
Uncommitted Costs	\$55,447,900	CMAR	Berry & Clay
Architect	GLS		

## SCHEDULE

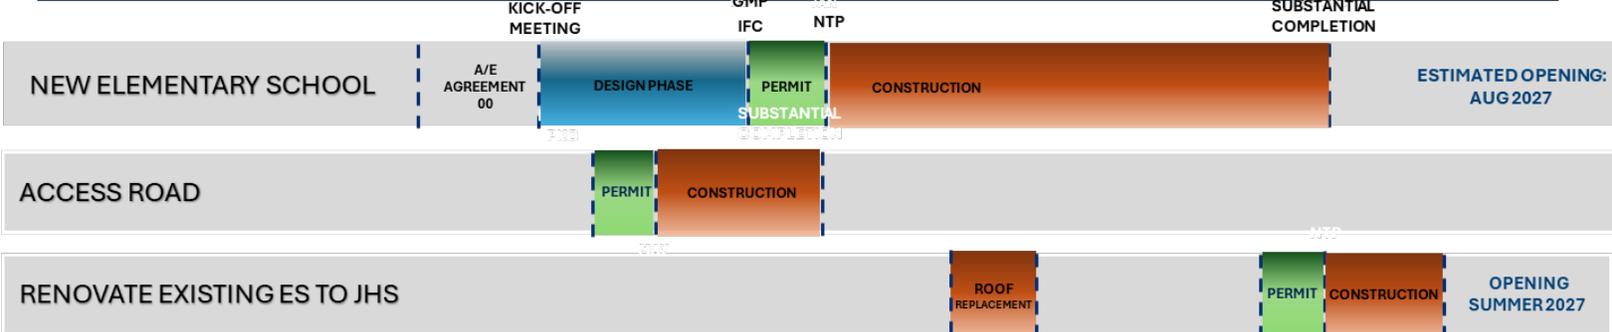

## PROJECT UPDATE

Project	Budget	Commitment	Cost to Date	Project Phase	Anticipated Completion Date
New Elementary	\$53,800,000	\$4,040,247	\$1,057,422	50% CD	Spring 2027
Access Road	\$2,500,000	\$206,392	\$125,500	100% CD	Winter 2025
Renovations to Existing ES	\$3,700,000	\$305,461	\$0	SD	Summer 2027

# STATUS UPDATES

- Access Road GMP approved
- Access Road Groundbreaking September 19, 2025, at 11am
- New ES Design Ongoing
  - 50% Construction Document Plans
  - Departmental Meetings:
    - Final IT Meeting
    - Final Hardware Meeting
    - Final Interior Finishes Meeting

# HIGHLIGHTS

- New ES Campus Renderings



Front Entrance Rendering



Cafeteria Rendering



Library Rendering
