

ANDERSON- SHIRO 2024 BOND PROGRAM

STATUS REPORT


May 2026

FINANCIAL UPDATE

Program Budget	\$60,000,000	Job Costs to Date	\$7,466,130
Commitments	\$43,183,206	Uncommitted Costs	\$16,816,794

Project	Budget	Commitment Costs	Job Cost to Date	Percent Complete	Project Phase	Anticipated Completion Date
Package 1 New Elementary School	\$53,800,000	\$40,592,882	\$5,552,843	10%	Construction	Spring 2027
Package 2 Access Road	\$2,500,000	\$2,265,770	\$1,839,505	74%	Construction	Spring 2026
Package 3 Renovations to Existing ES	\$3,700,000	\$324,553	\$73,781	2%	Design	Summer 2027

Schedule

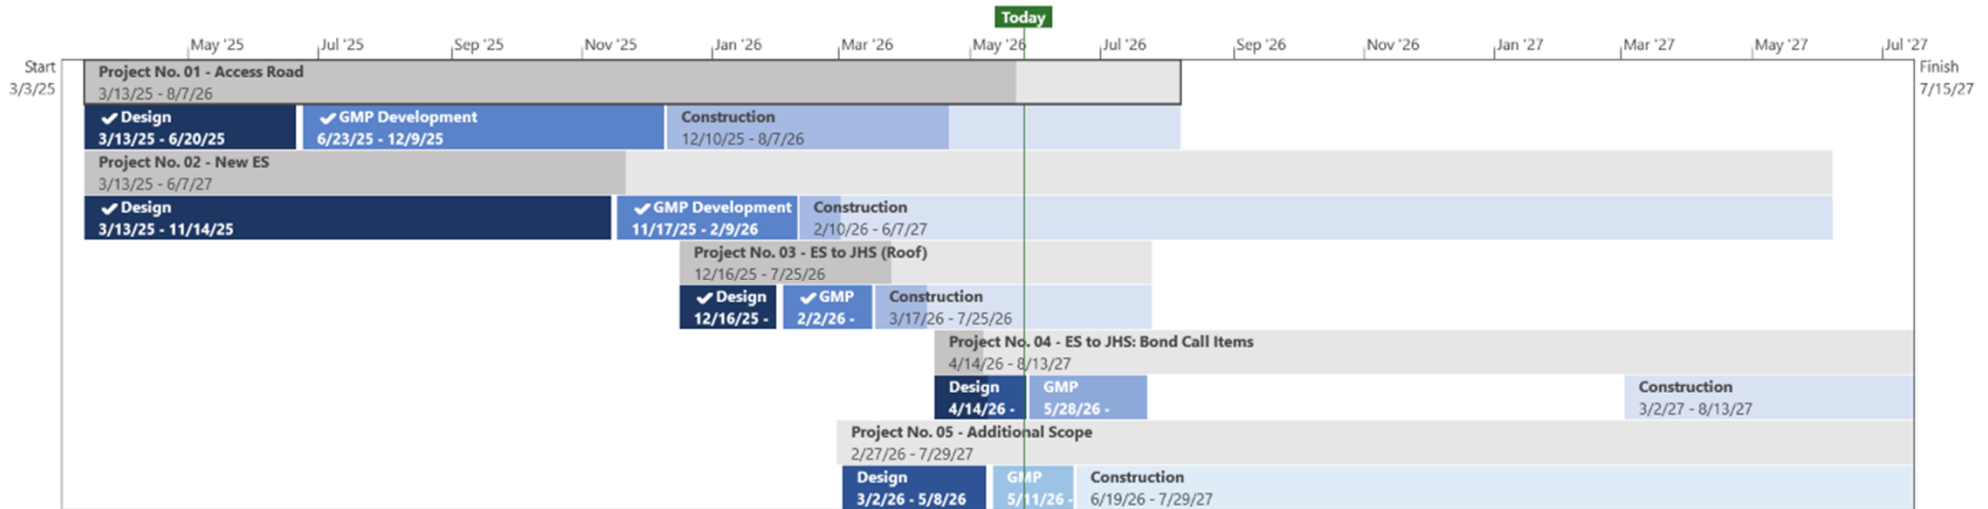

ASCISD 2024 Bond



CUMMING GROUP
GALLAGHER



STATUS UPDATES

- New Elementary School
 - Underground utilities ongoing
 - Grade beams have begun; first pour May 21
- Access Road
 - Widening of FM 149 to begin June 1
 - Substantially complete; punch list in progress
 - Road will open to general public August 2027
- Renovations to Existing ES
 - Reroof began May 4th
 - Construction Documents for locker rooms, vestibule, and restrooms to be completed June 18.

PROJECT PHOTOS & RENDERINGS



Grade beam concrete pour



Reroof over ES locker rooms

