

ANDERSON- SHIRO 2024 BOND PROGRAM

STATUS REPORT


June 2026

FINANCIAL UPDATE

Program Budget	\$60,000,000	Job Costs to Date	\$9,479,408
Commitments	\$44,281,771	Uncommitted Costs	\$15,718,229

Project	Budget	Commitment Costs	Job Cost to Date	Percent Complete	Project Phase	Anticipated Completion Date
Package 1 New Elementary School	\$53,800,000	\$40,631,320	\$7,566,121	14%	Construction	Spring 2027
Package 2 Access Road	\$2,500,000	\$2,265,770	\$1,839,505	74%	Construction	Spring 2026
Package 3 Renovations to Existing ES	\$3,700,000	\$1,384,680	\$73,781	2%	Design	Summer 2027

Schedule

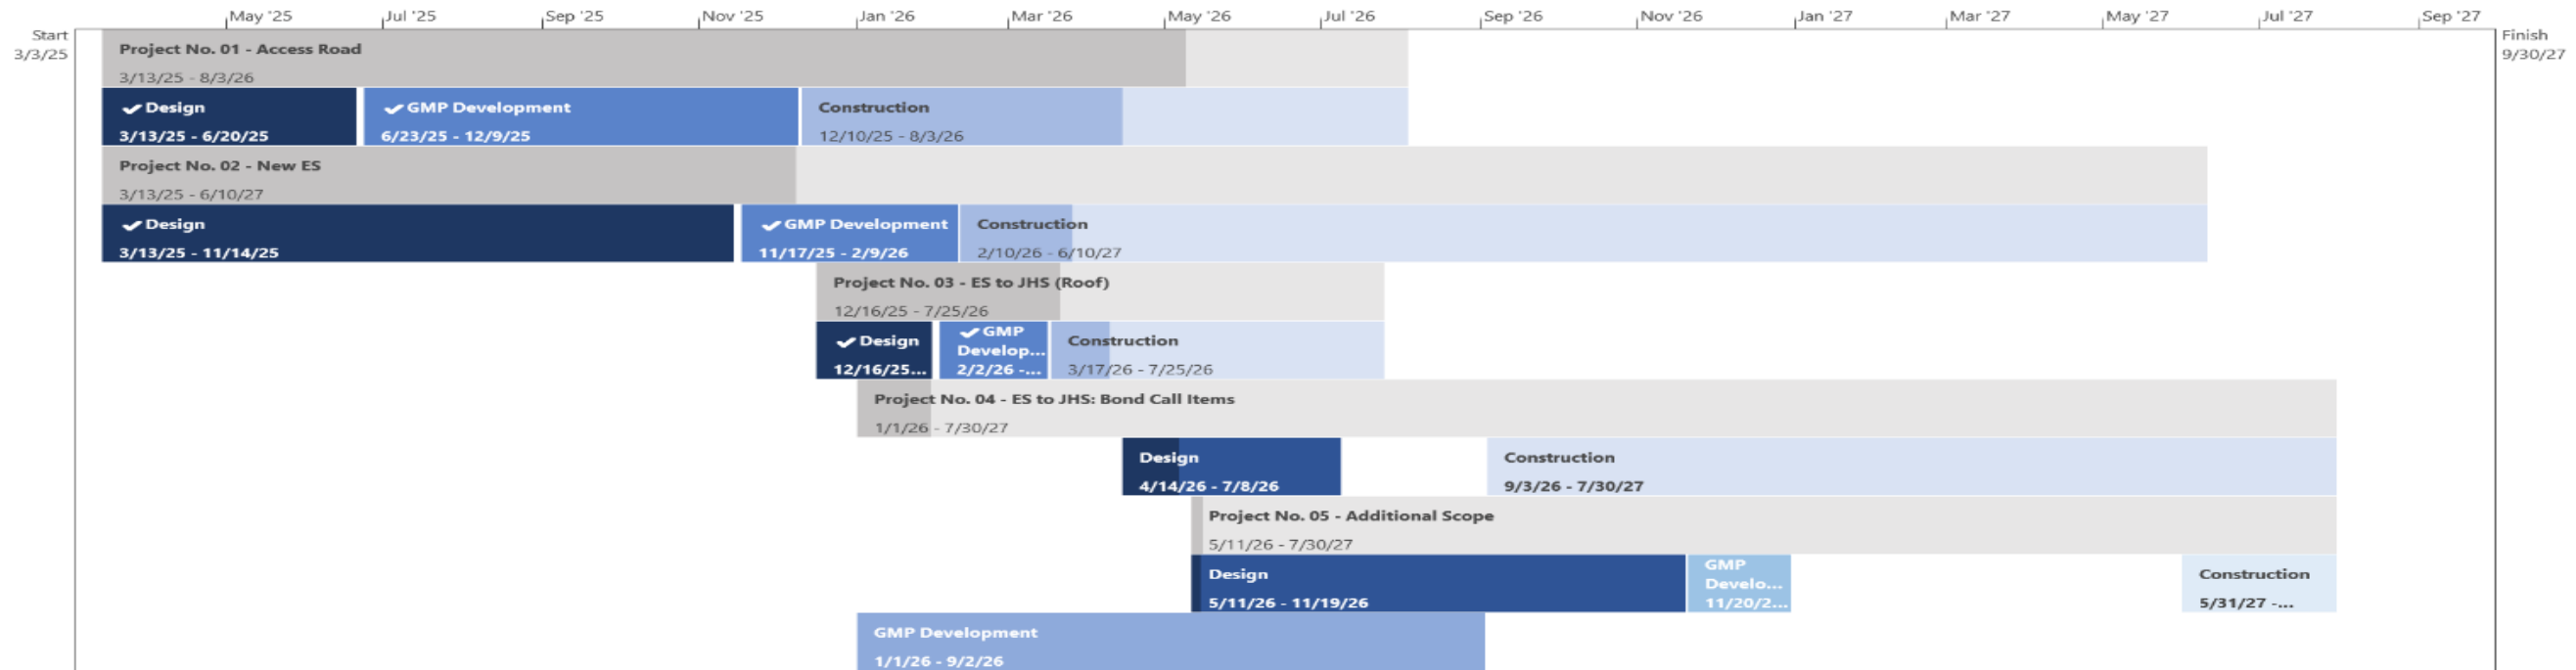

ASCISD 2024 Bond



STATUS UPDATES

- New Elementary School
 - Underground utilities ongoing
 - Foundations have been poured in sections A through D
- Access Road
 - Widening of FM 149 to begin June 1
 - Substantially complete; punch list in progress
- Renovations to Existing ES
 - Reroof began May 4th
 - Construction Documents for locker rooms, vestibule, and restrooms in process, to be completed in July

PROJECT PHOTOS & RENDERINGS



Area C Foundation (Cafeteria)



Cafeteria Concrete Pour



Reroof over Current Elementary School

