

# ANDERSON- SHIRO 2024 BOND PROGRAM

## STATUS REPORT


### April 2026

#### FINANCIAL UPDATE

Program Budget	\$60,000,000	Job Costs to Date	\$3,951,378
Commitments	\$43,153,206	Uncommitted Costs	\$16,846,794

Project	Budget	Commitment Costs	Job Cost to Date	Percent Complete	Project Phase	Anticipated Completion Date
Package 1 New Elementary School	\$53,800,000	\$40,592,882	\$3,562,077	7%	Construction	Spring 2027
Package 2 Access Road	\$2,500,000	\$2,250,770	\$1,056,894	43%	Construction	Spring 2026
Package 3 Renovations to Existing ES	\$3,700,000	\$324,553	\$43,089	1%	Design	Summer 2027

#### Schedule

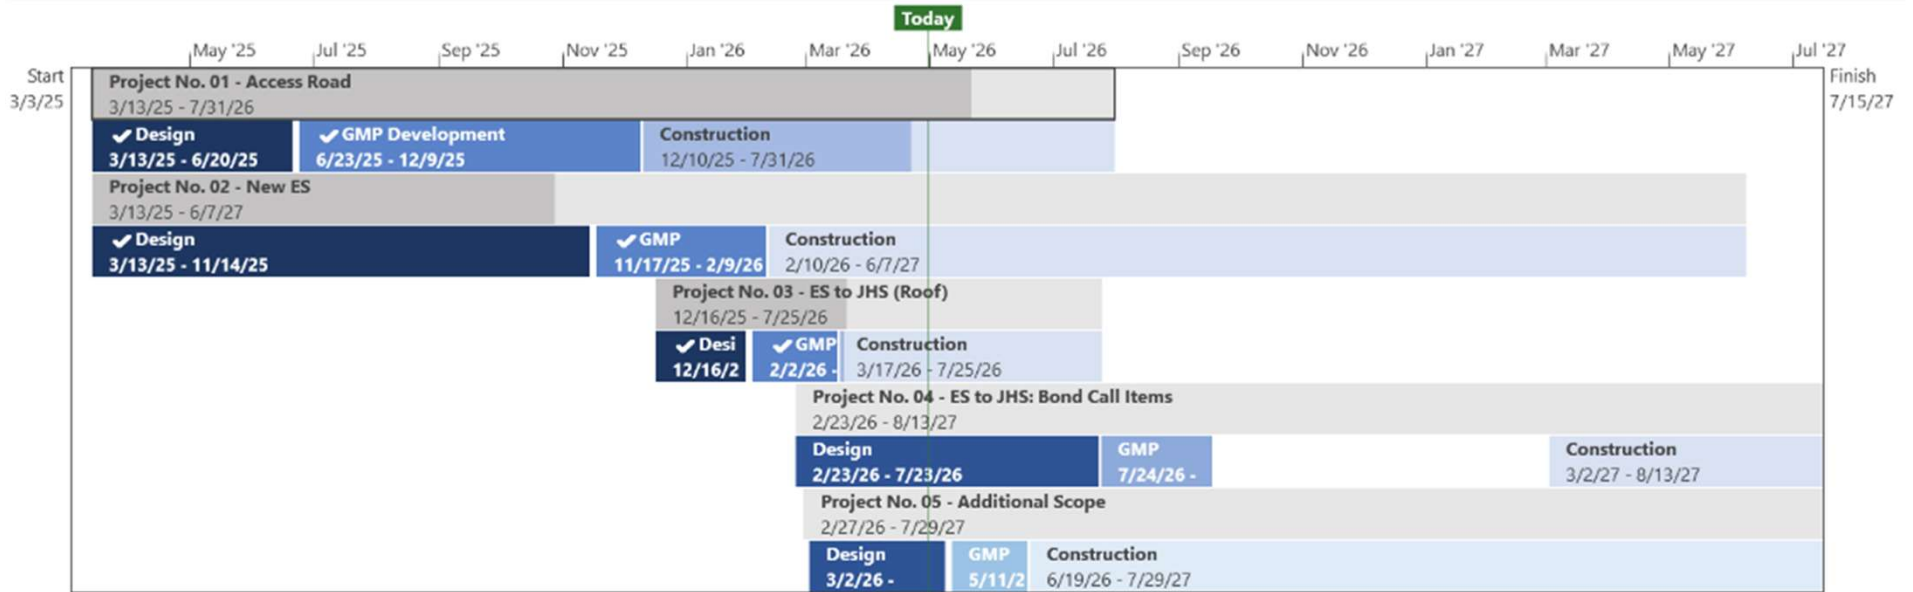

ASCISD 2024 Bond



CUMMING GROUP  
GALLAGHER



## STATUS UPDATES

- New Elementary School
  - Mobilization began Feb. 11
  - Site work on-going
  - Select fill on-going until June 1
- Access Road
  - Compaction, rebar, forms, concrete pours complete
  - Project roughly 95% complete
  - Road will open to public August 2027
- Renovations to Existing ES
  - Demolition to begin May 4<sup>th</sup>, 2026 over the locker rooms

## PROJECT PHOTOS & RENDERINGS



**New ES footprint with select fill**



**New ES Site Work**

