

ANDERSON- SHIRO 2024 BOND PROGRAM

STATUS REPORT


September 2026

FINANCIAL UPDATE

Program Budget	\$60,000,000		Job Costs to Date	\$15,440,803`
Commitments	\$44,298,366		Uncommitted Costs	\$15,701,634

Project	Budget	Commitment Costs	Job Cost to Date	Percent Complete	Project Phase	Anticipated Completion Date
Package 1 New Elementary School	\$53,800,000	\$40,647,915	\$12,699,994	24%	Construction	Spring 2027
Package 2 Access Road	\$2,500,000	\$2,265,770	\$1,839,505	74%	Construction	Spring 2026
Package 3 Renovations to Existing ES	\$3,700,000	\$1,384,680	\$901,354	24%	Design	Summer 2027

Schedule

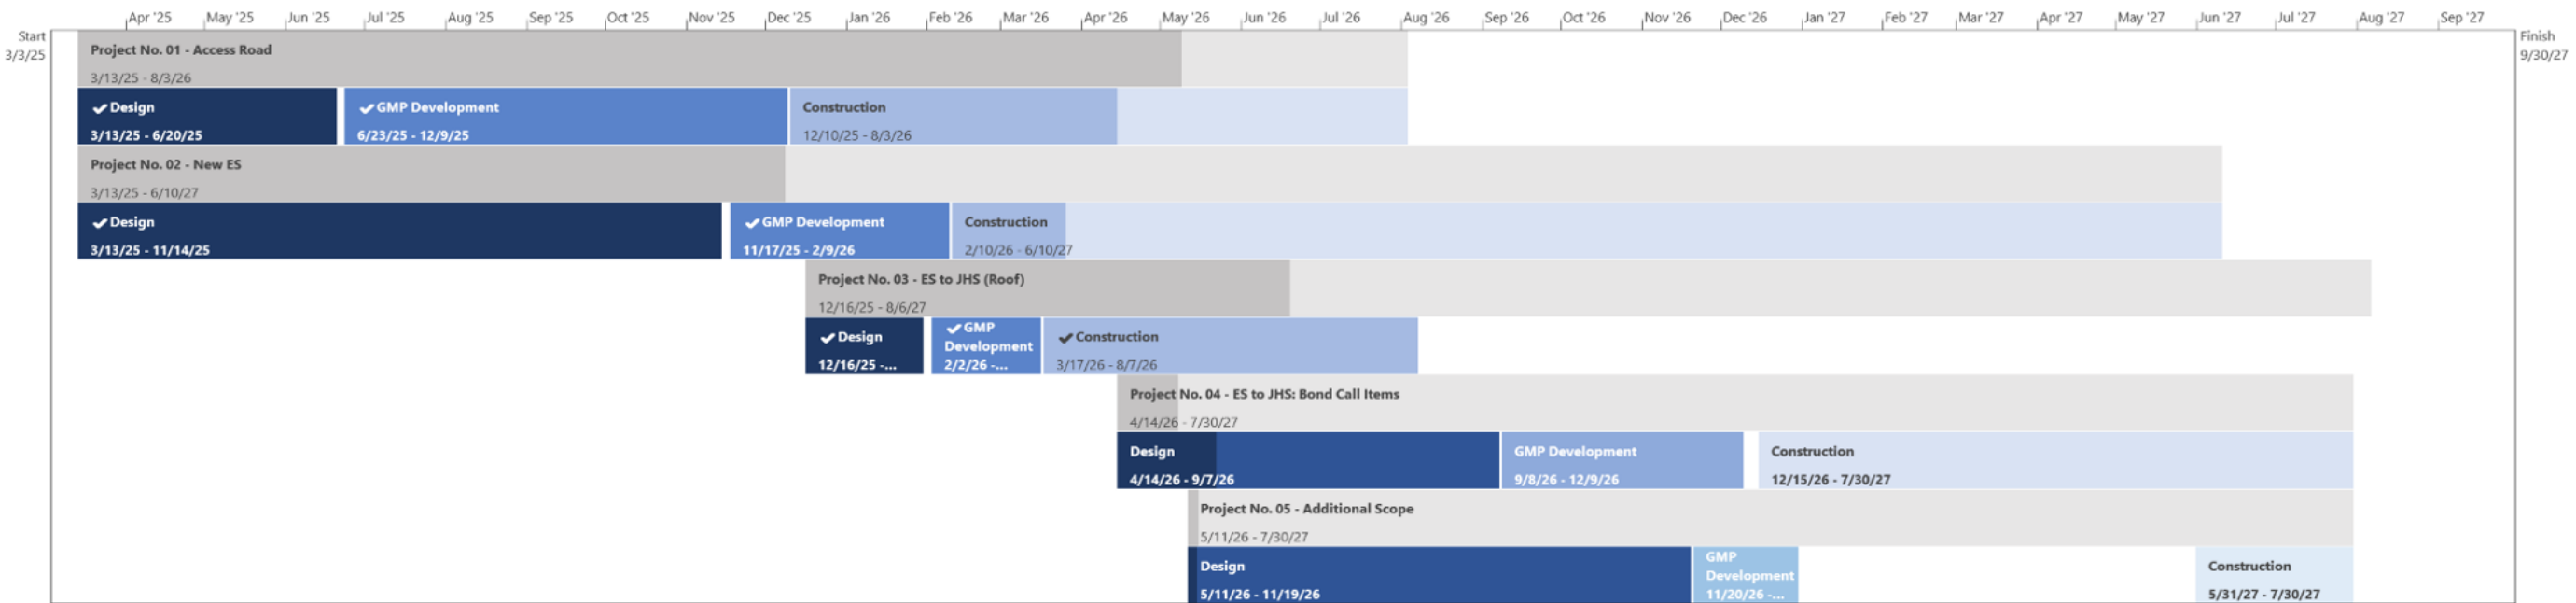

ASCISD 2024 Bond



STATUS UPDATES

- New Elementary School
 - CMU installation: In Progress
 - Metal stud installation: In Progress
 - Roof insulation/decking installation: In Progress
- Access Road
 - Construction complete and closeout in progress
- Renovations to Existing ES
 - Re-Roof completed August 7th
 - Construction Documents submitted by GLS for review on September 16th

PROJECT PHOTOS & RENDERINGS



FM-149 Road Widening



New ES – Insulation Panels



New ES- Paving Pour

